



Basing Consolidation Update

MNC-I, C-3 Plans & Policy
As of: 08 JUL 05





Basing Requirement and Endstate

Requirement:

- Base forces to support the MNF-I Campaign plan

Basing End State:

- Coalition footprint consolidated to 4 Bases: Balad (Anaconda), Al Asad, Q-West and Tallil (Adder)
- OIF Contingency Operating Bases (COB) located at Balad, Al Asad, Tallil and Irbil
- Bases desired by the ISF are transferred to Ministry of Interior or Defense control
- Bases not needed by the ISF are closed and returned to the Government of Iraq through the Ministry of Finance
- Minimize basing costs while supporting the mission



Basing Guidance

- Basing plan meets operational demands
- Execution of basing plan occurs in accordance with the Campaign Plan
- Establish COBs in each of the three cultural areas of Iraq: Sunni, Shia and Kurd
- Expedite hand over of symbols of National sovereignty, palaces
- Develop contingency plans for early hand back of Palaces (returned without any remnants of Coalition occupation)
- Position bases to influence key urban areas; COBs not to be located within key urban areas
- Ensure basing plan conforms to the CENTCOM Sandbook contingency basing guide-lines
- Retain flexibility in basing
- Transfer Coalition bases to the ISF in the first instance
- Ensure basing allows for sufficient force projection to counter any potential security scenarios



METHODOLOGY

- Analysis of TRA leads to identification of trained and ready IZ Forces which relates to the offramp strategy.
- **Conditions-based process. MSCs manage their consolidation process.**
- MSCs nominate bases for closure. MNC-I validates the requests to consolidate; set priorities and apportion resources
- MNC-I has formed the BRAC4IRAQ Team
- Battlespace Management Board, chaired by CoS, Tuesdays 10-1200
- Basing workgroup (action officer level), Saturdays 13-1500
- Within MNC-I
 - C3 coordinates “Basing Issues”
 - C7 is responsible for the facility prep & turnover including environmental
 - C4 is responsible for managing installation property transfer & life support services
- LOGCAP, KBR, DCMA, and C8 are involved members of the team
- Basing considerations are injected into all operational planning efforts



Planning Considerations

▶ As long as Coalition Partners remain, they will remain in.....

 UK : BAS*, SLB**, Um Quasr Port, Basrah Palace

 ITA: Mittica

 JPN: Samawah

 ROK: Zaytun

 UKR: Delta

 POL: Echo

▶ IZ/AMEMB will require a security element. It will remain at FOB Prosperity

▶ As long as MNC-I has maneuver forces in Baghdad we will occupy Victory & Tadj

▶ Requirement for embedded MiTTs will limit consolidation in some areas

▶ Model of 100 days required for base consolidation

UNCLASSIFIED

UNCLASSIFIED



(b)(1)1.4a, (b)(1)1.4b



UNCLASSIFIED

Page 7 redacted for the following reason:

(b)(1)1.4a, (b)(1)1.4b

Pending Closure/ Handover → Dec 2005


<u>MNF-W</u>	
Hotel	28AUG
Lima	01OCT

<u>MND-NC</u>	
Scunion	15JUL
Dagger	31JUL
Omaha	31JUL
Barbarian	30SEP
Cobra	01OCT
O’Ryan	30OCT
Danger	01DEC

<u>MND-B</u>	
Honor	28SEP

<u>MND-CS</u>	
Zulu	01SEP

<u>MND-SE</u>	
Qurna	15JUL
Chindit	01OCT
OSB	01OCT

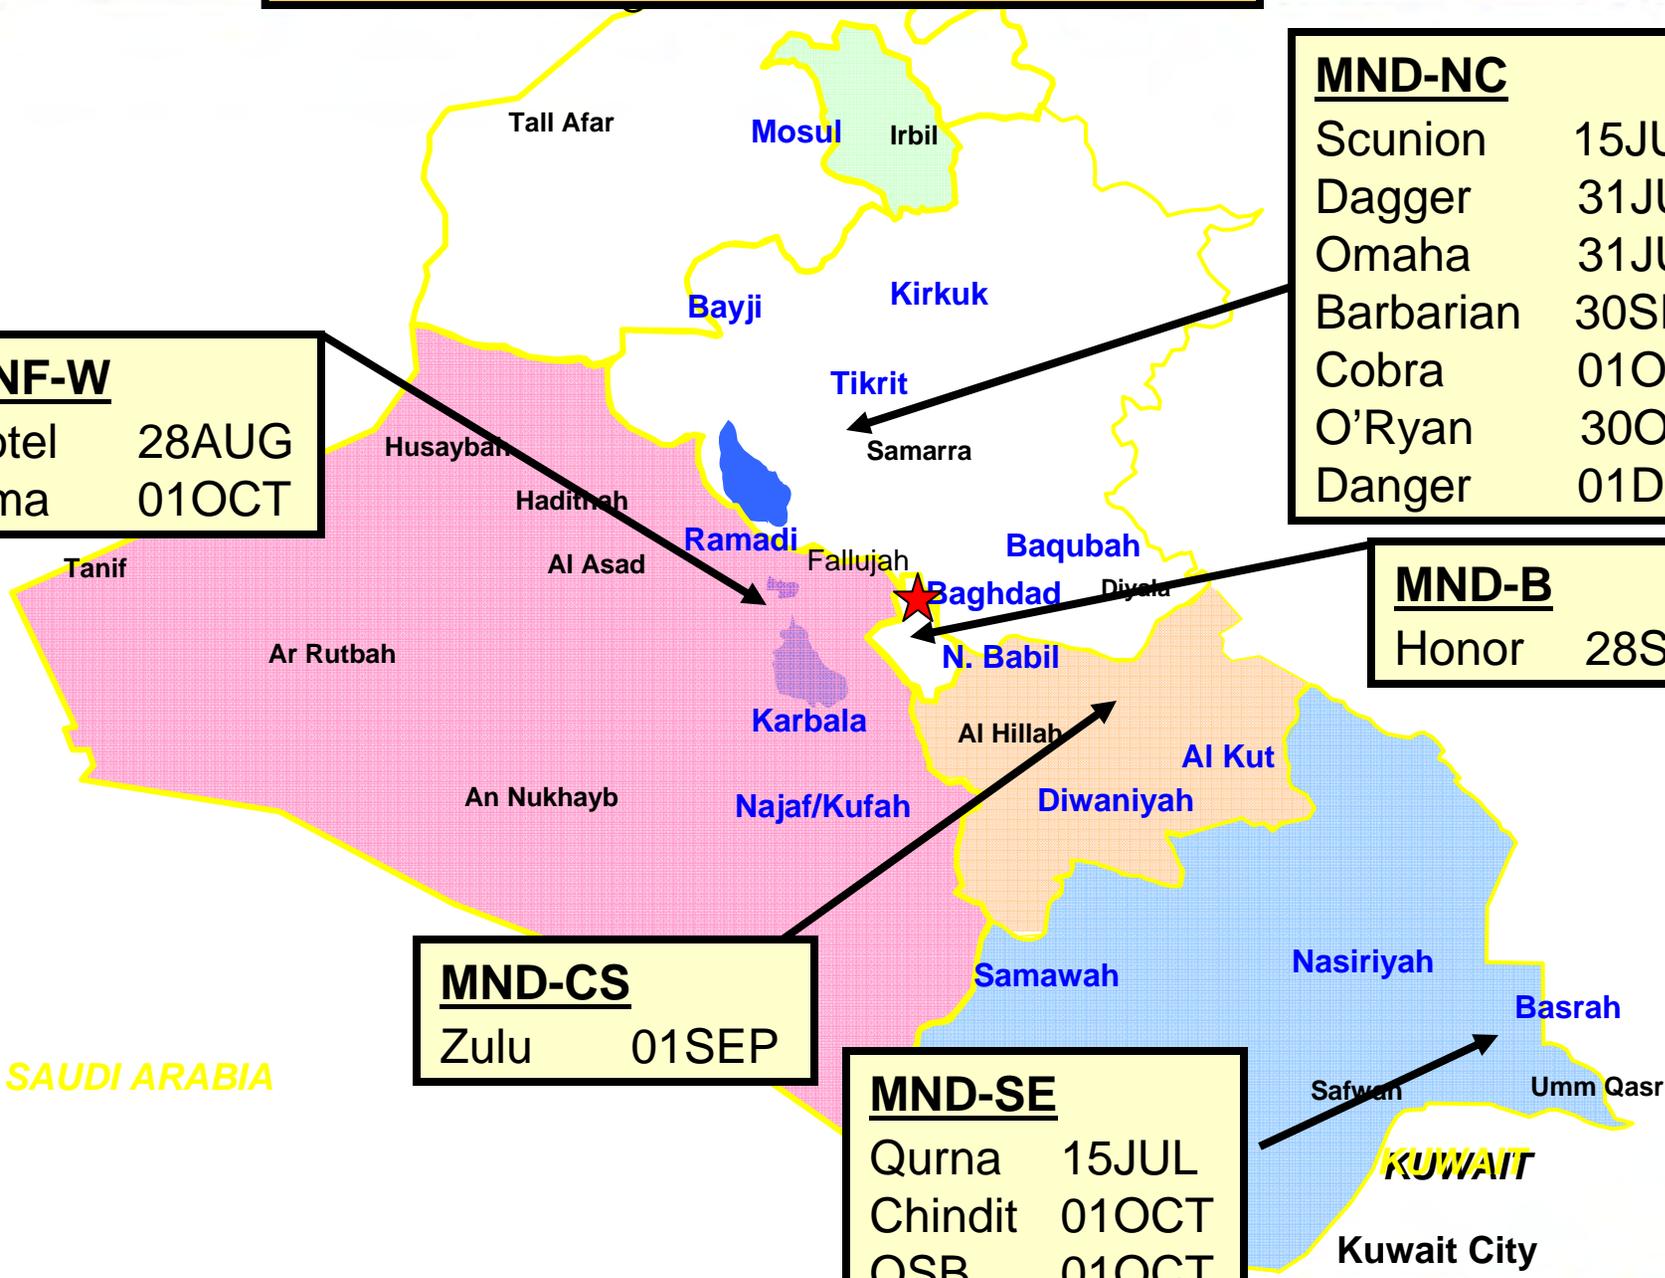

SAUDI ARABIA

KUWAIT

Kuwait City

★ Condition-based Process


SECRET REL USA, IRQ ,and MCFI

14 Bases projected to close by DEC 05

8 will transfer to the Iraqi Army

Palace Complexes
Dagger/Danger/Courage

Basing Operational Timeline

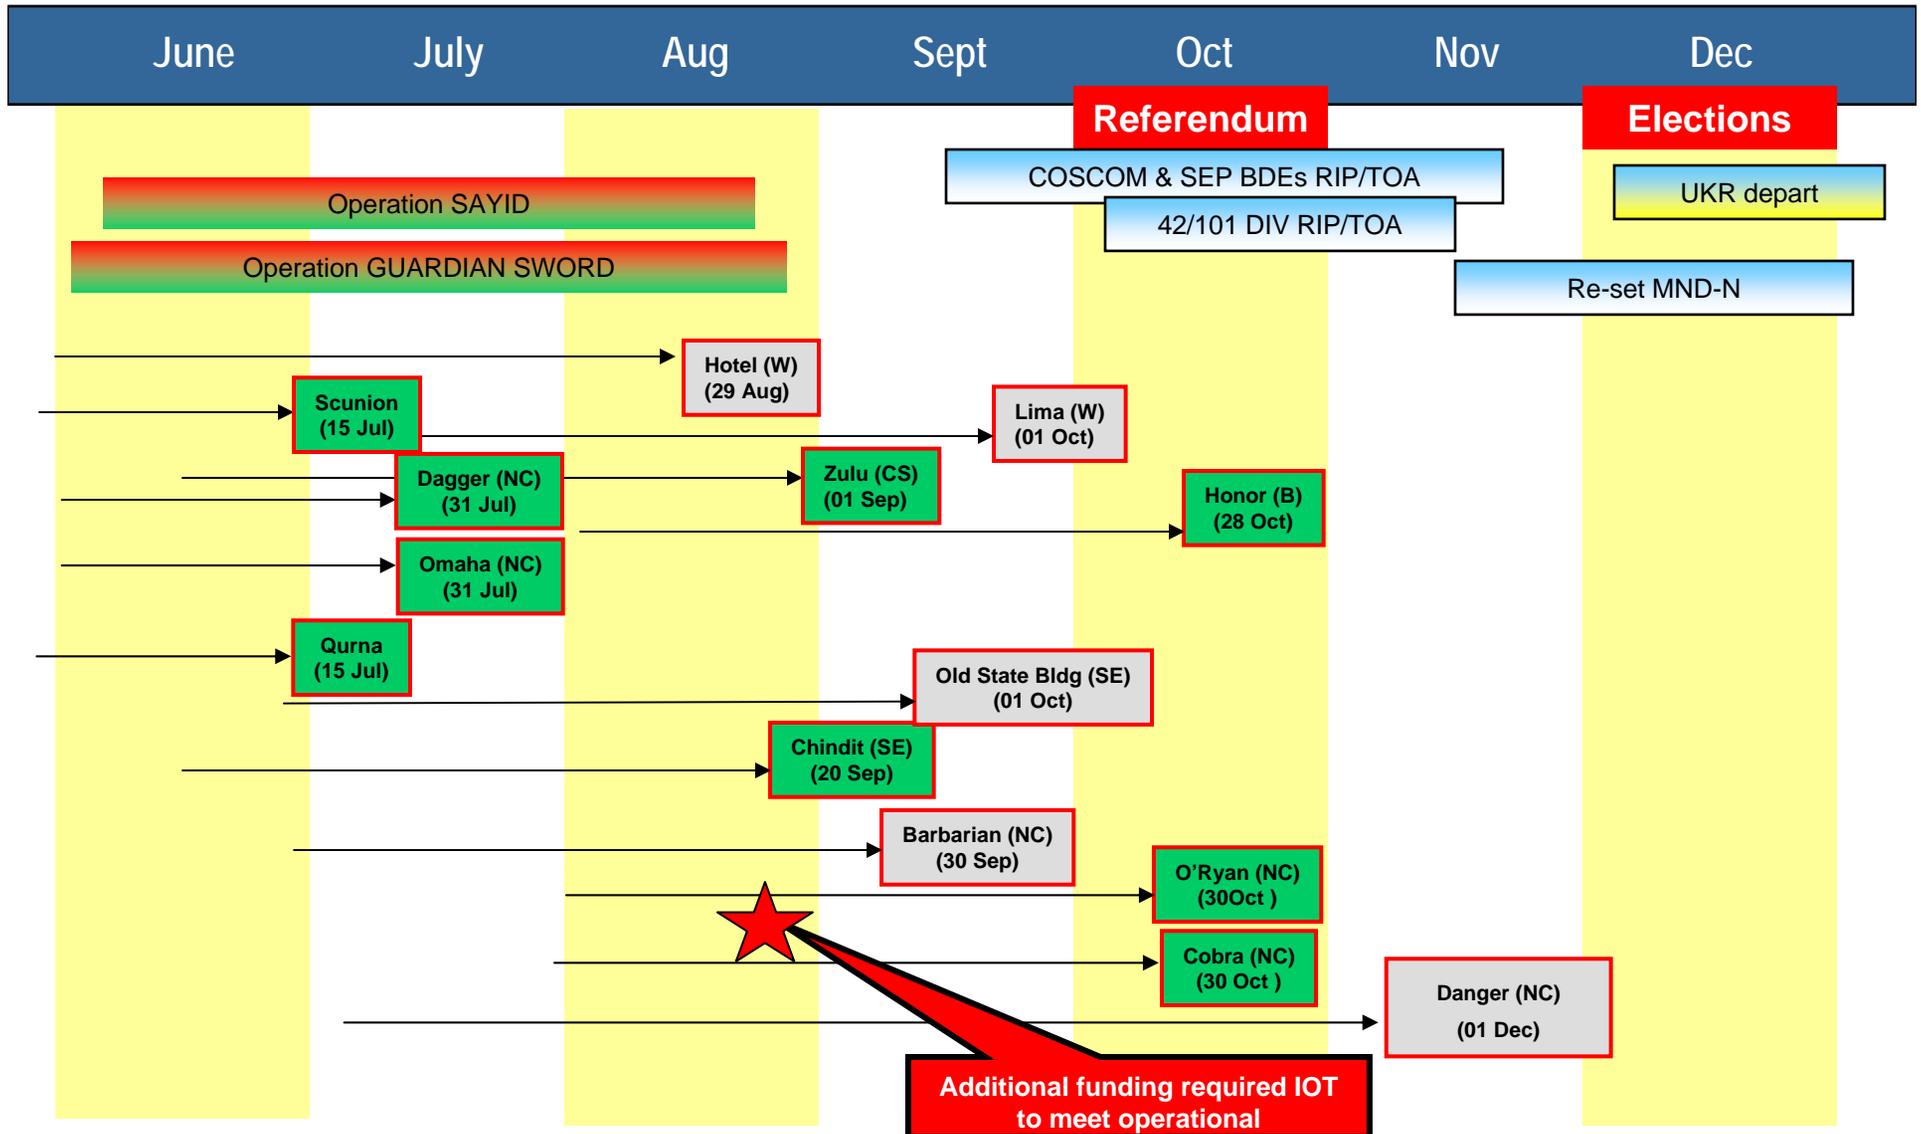

UNCLASSIFIED



MNC-I Basing Posture FEB 2006

(b)(1)1.4a, (b)(1)1.4g

UNCLASSIFIED

UNCLASSIFIED



MNC-I Basing Posture AUG 2006

(b)(1)1.4a, (b)(1)1.4g

UNCLASSIFIED

BRAC4IRAQ

FISCAL REPORT

Estimate as of 08JUL05

COST SUMMARY (\$M)

Closing Costs	44.8
Remediation (estimate)	25.0
Consolidation Costs (1 yr)	352.8
Total Costs	422.6
Funded to date	65.2
Remaining Costs	357.4

Closures Pending (<100 days)

<u>Name</u>	<u>MND</u>	<u>Iraqi</u>	<u>MiTT</u>	<u>Disposition</u>	<u>Transfer</u>	<u>JARB</u>	<u>Requirement</u>	<u>Funded</u>
Omaha	NC	1/1/4	No	Ramagen	JUL	NR	0.0	
Hotel	W	Bde HQ	No	Dogwood/Duke	AUG	Yes	23.6	12.5
Zulu	CS	3/3/8	No	Redeploy	SEP	No	2.1	2.1
Scunion	NC	1/1/5	No	MNF-W	JUL	NR	0.0	
Dagger	NC	4 DIV	Yes	Speicher	JUL	NR	0.0	
Al Qurna	SE	1/1/10	No	Redeploy	JUL	No	0.5	0.5
Barbarian	NC	IPS	No	Warrior	SEP	No	4.1	1.8
Honor	B	5 BDE	Yes	Liberty	SEP	No	37.0	15.4
Lima	W			Kalsu	OCT	Yes	19.2	12.0

Closure Nominations

<u>Name</u>	<u>MND</u>	<u>Iraqi</u>	<u>MiTT</u>	<u>Disposition</u>	<u>Transfer</u>	<u>JARB</u>	<u>Requirement</u>	<u>Funded</u>
Chindit	SE	2/1/10	No	SLB	OCT	No	6.7	
OSB	SE		No	BAS	OCT	No	6.9	
O'Ryan	NC	30 BDE	Yes	TBD	OCT	No	28.0	
Cobra	NC	3/2/5	Yes	TBD	OCT	No	20.7	
Danger	NC		No	Speicher	DEC	No	116.2	
Courage	NW			Redeploy	JAN	No	2.0	
Abu Naji	SE	1/4/10	No	Redeploy	JAN	No	3.7	
Midland	NC		No	Redeploy	AUG	No	0.6	

Expansions

<u>Name</u>	<u>MND</u>	<u>Iraqi</u>	<u>MiTT</u>	<u>Disposition</u>	<u>Transfer</u>	<u>JARB</u>	<u>Requirement</u>	<u>Funded</u>
Sykes	NW			Expansion	0	Yes	65.3	15.0
Liberty	B			Expansion	0	Yes	23.7	2.0
SinBiajRab	NW				0	Yes	2.9	1.5
Stryker	B			Expansion	0	Yes	34.6	2.4


Issues

- Funding is required IOT proceed with closures, transfers and consolidations which will allow us to put the right forces in the right location, build ISF capability & capacity, ultimately resulting in an incremental off-ramp of coalition forces.
- Determining GOI tenants for Basecamps that have not been identified for transfer to MoI or MoD. Priority is FOB Danger (01 DEC 05) and FOB Courage (01JAN 06).
- Future of Victory Base Complex, including intent and associated timeline, must be determined.

Page 14 redacted for the following reason:

(b)(1)1.4a, (b)(1)1.4b


Conditions-Based Model for Consolidation (MND-NC)

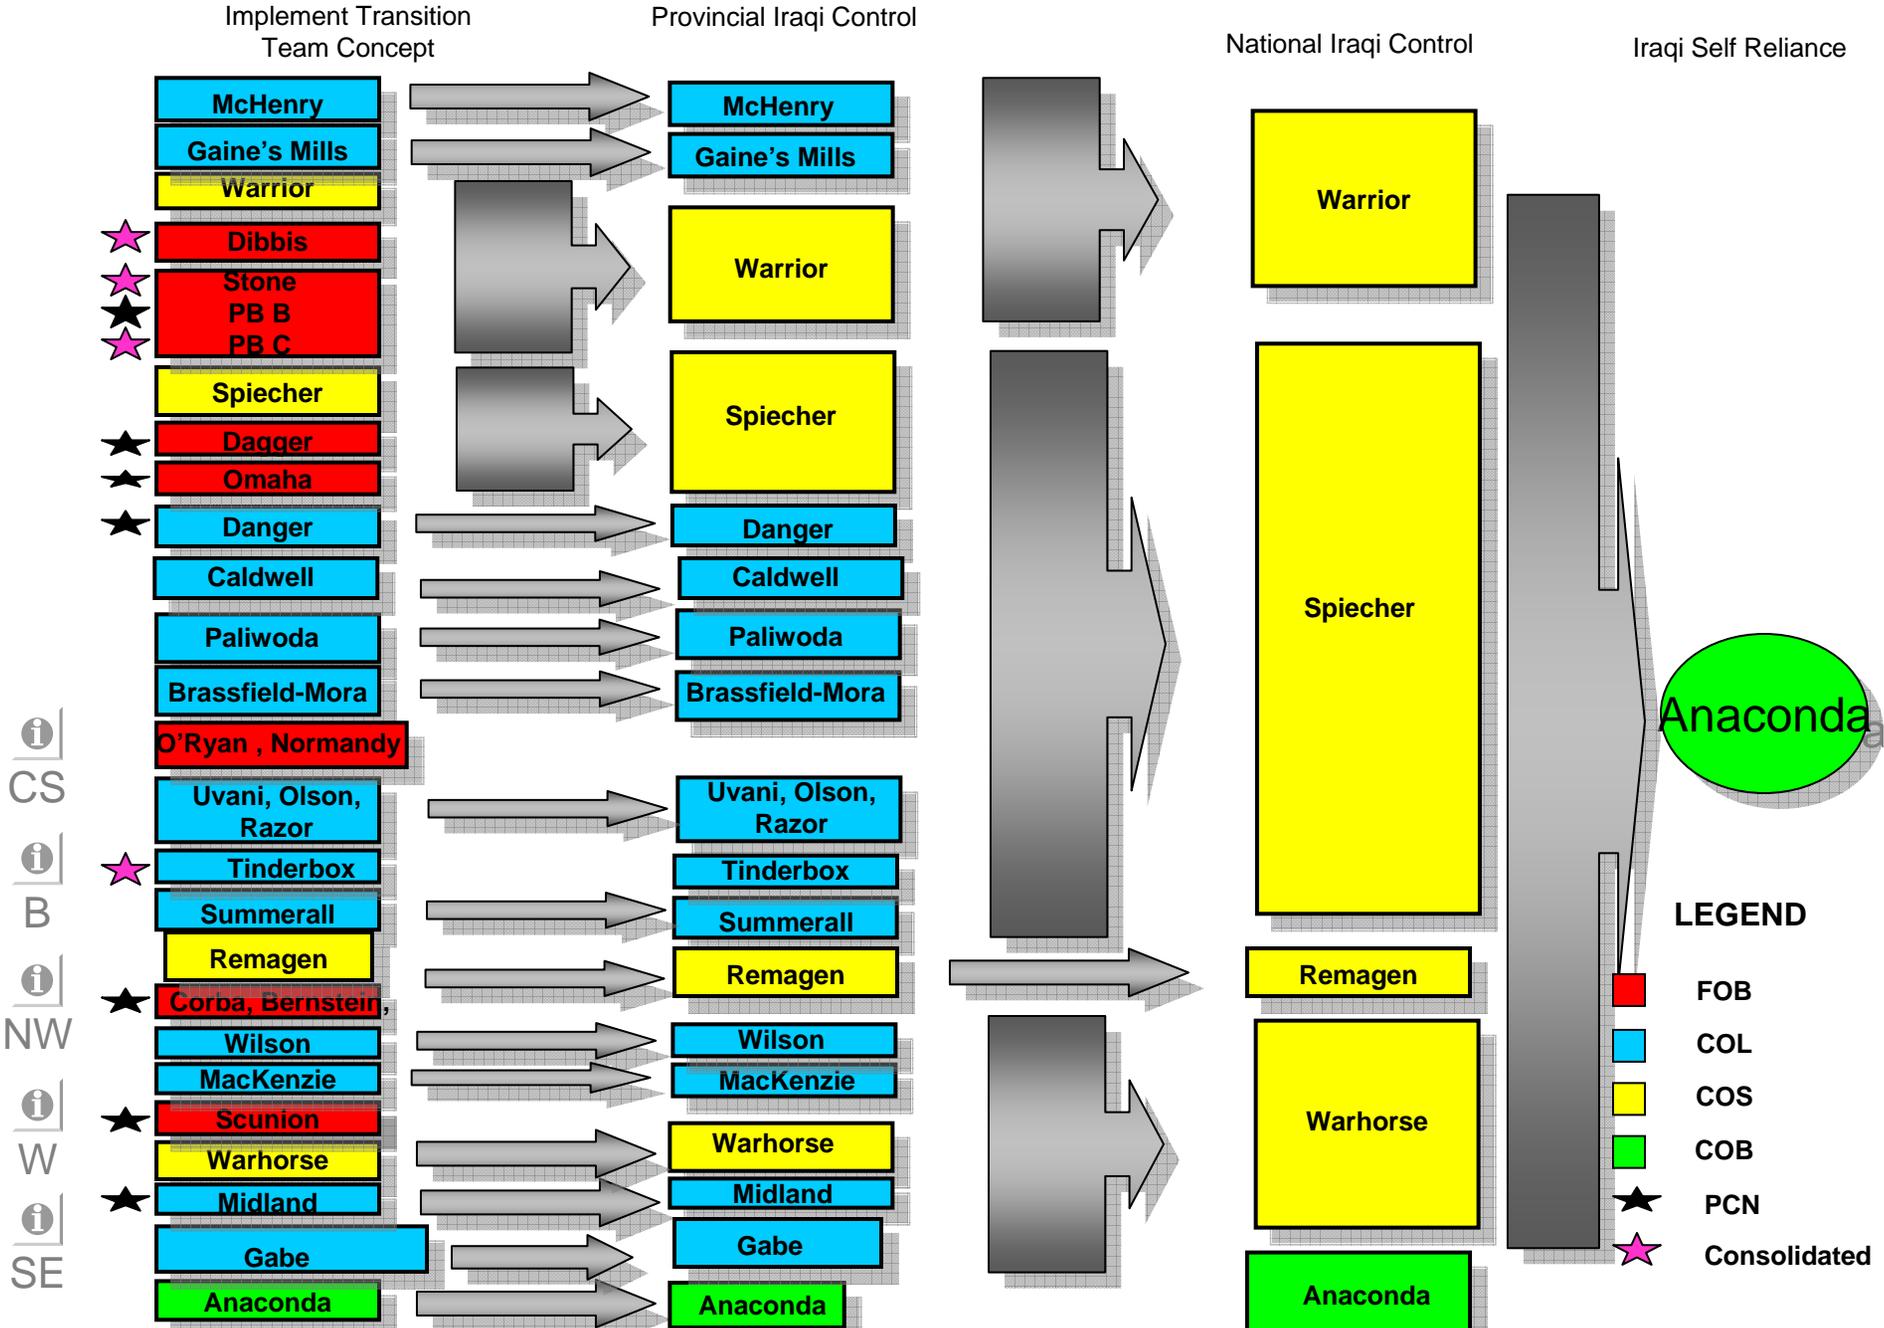

Base Closure Timeline

The Base Consolidation Timeline


- Requires 100 days of backwards planning
- Forecasts will be discussed in new Basing Operations Working group

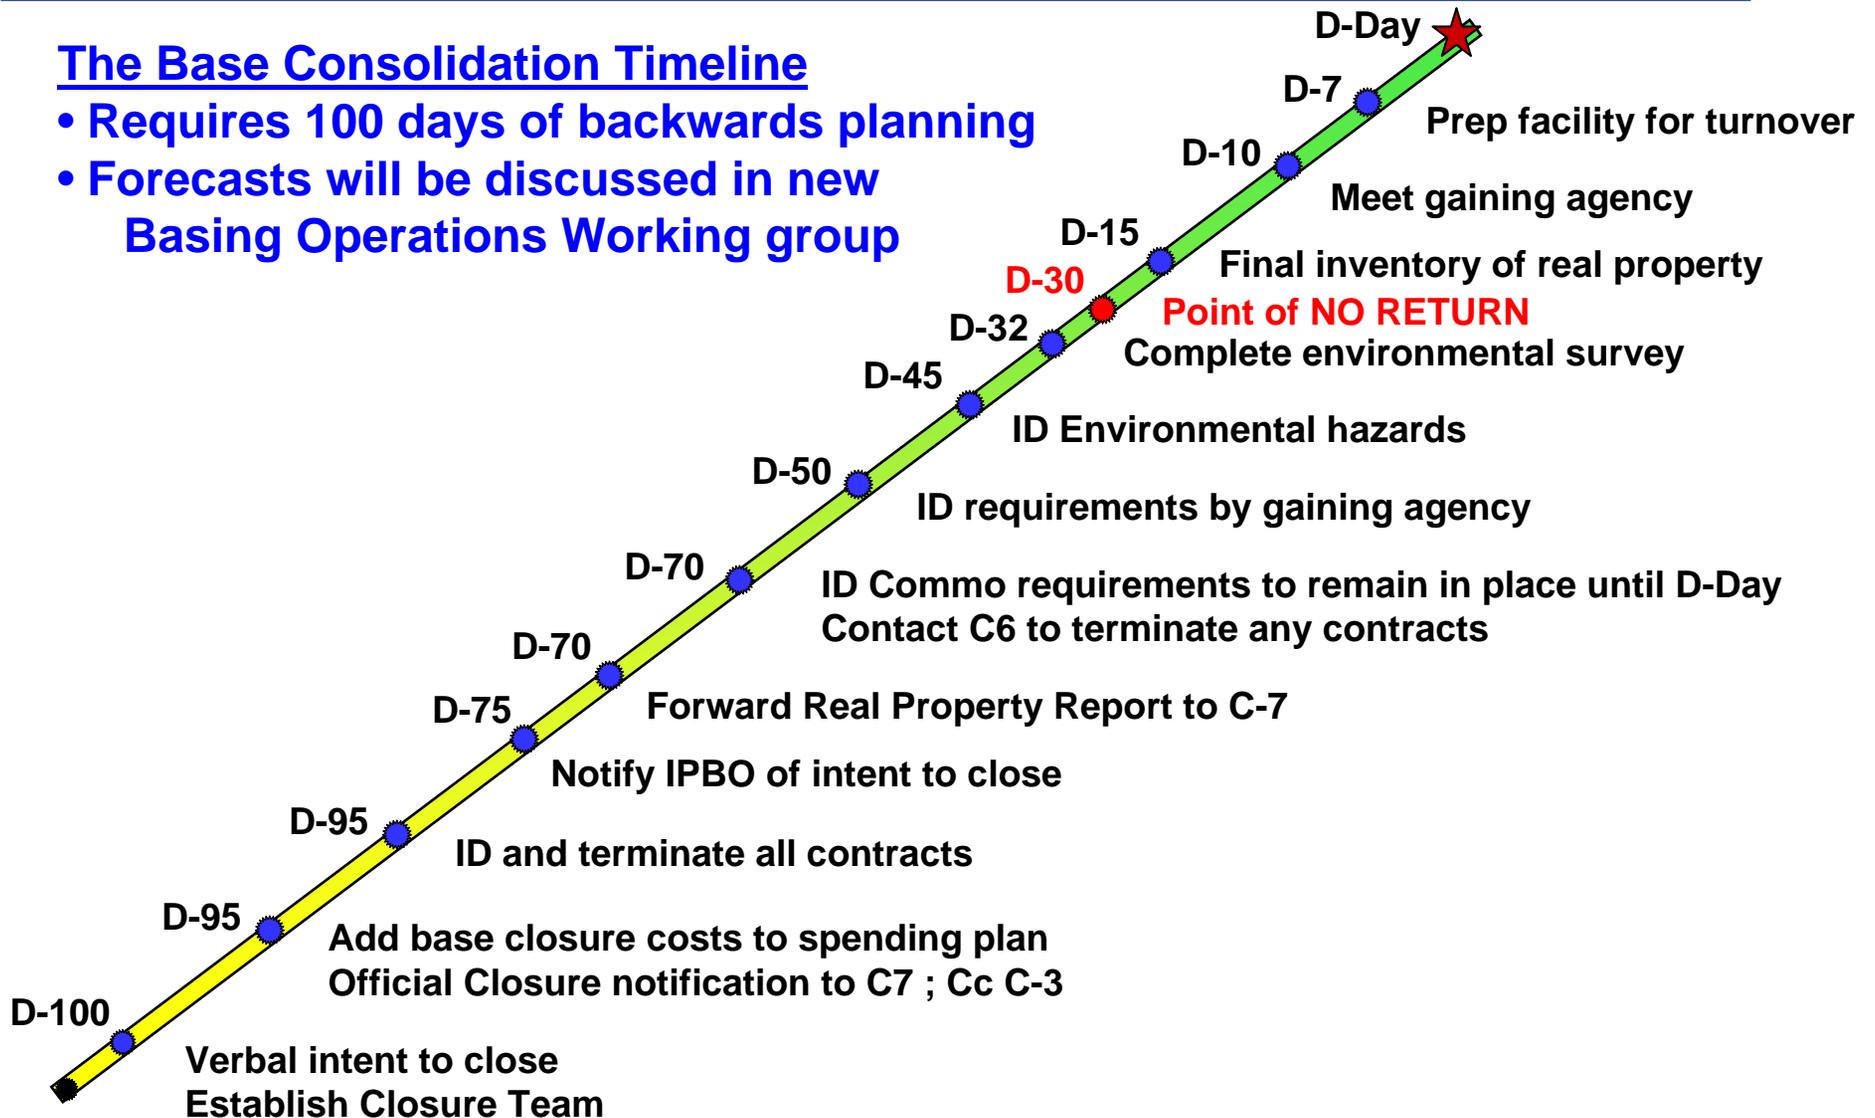



Base Closure Timeline

FOB OMAHA
Transfer NLT 31 JUL 05
To: 1Bn/1Bde/4Div
Issues: None at this time

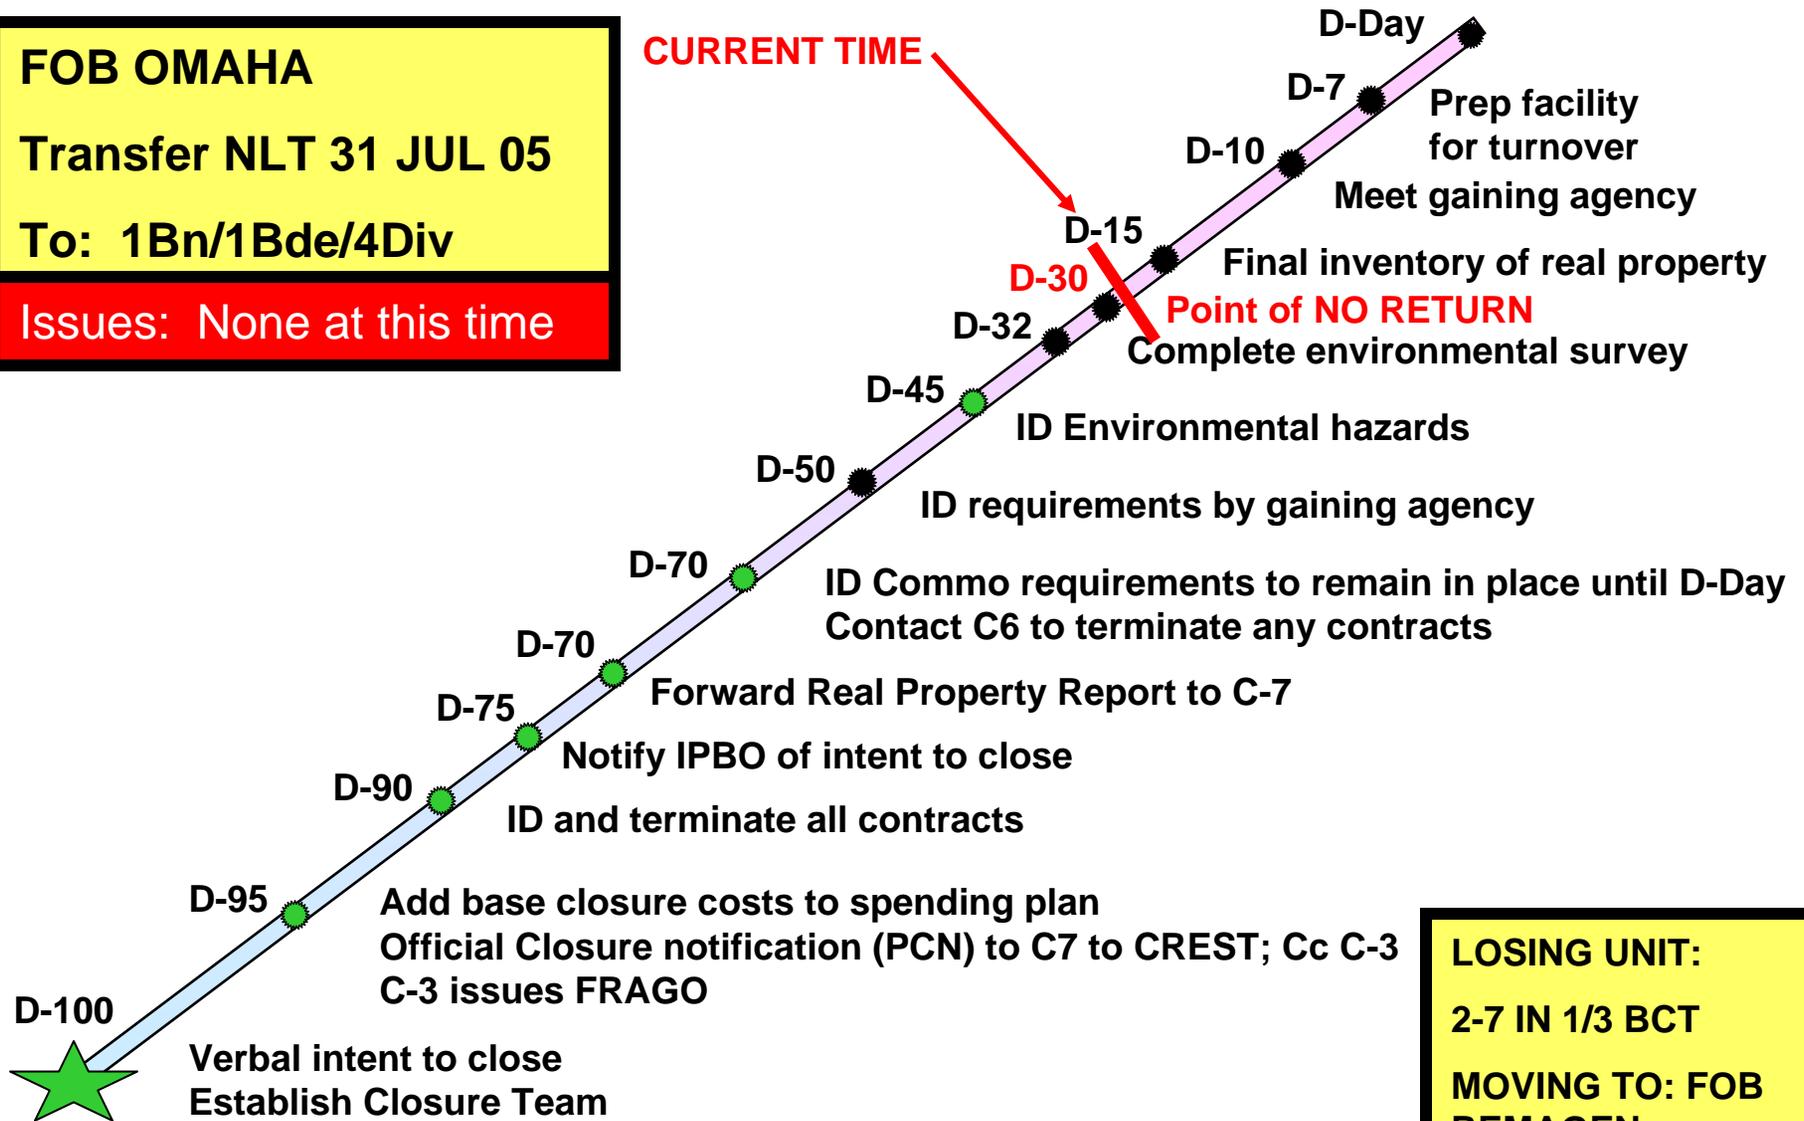


LOSING UNIT:
2-7 IN 1/3 BCT
MOVING TO: FOB
REMAGEN



Base Closure Timeline

FOB DAGGER
 Transfer NLT 31 JUL 05
 To: 4 IA Div HQs
 Issues: None at this time

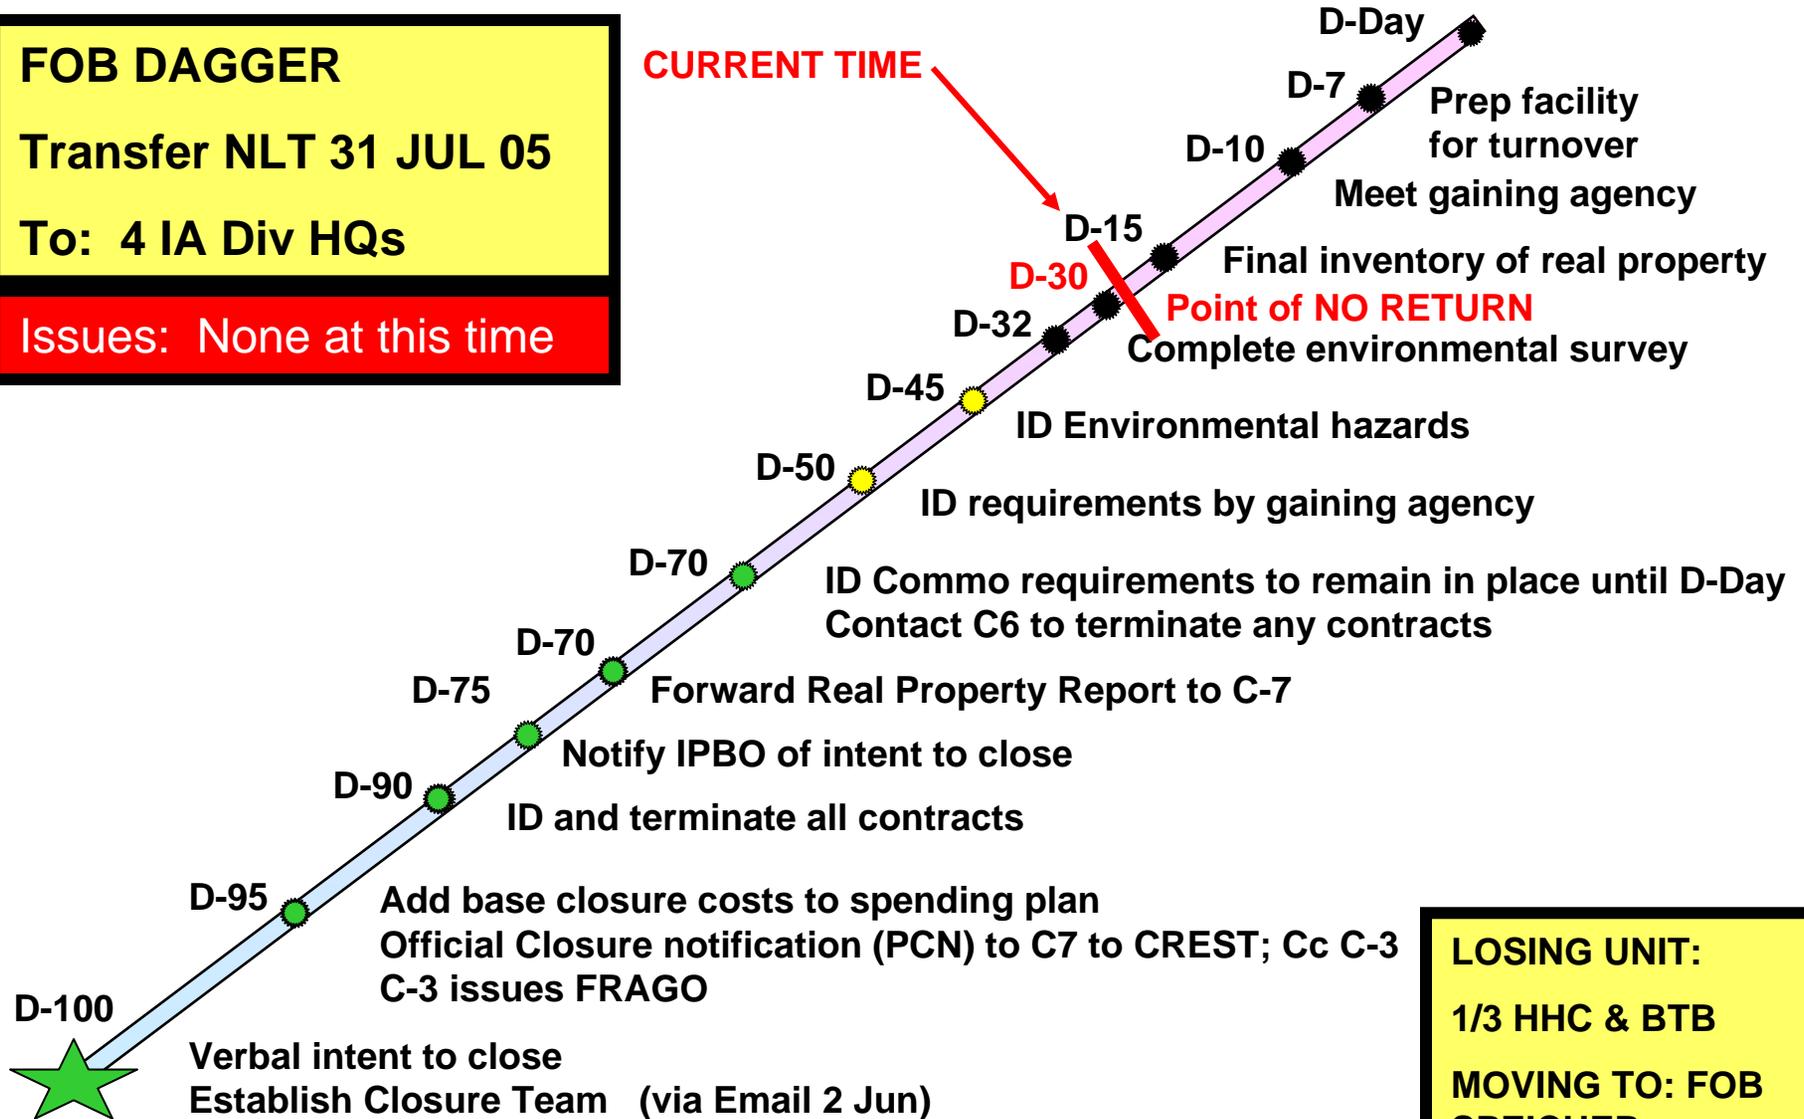

LOSING UNIT:
 1/3 HHC & BTB
MOVING TO: FOB
SPEICHER

Base Closures & Transfers June 2005 – January 2006

JUNE	JULY	AUGUST	SEPTEMBER
√ Stone √ Dibbis √ Crazyhorse	Omaha Scunion Dagger Qurna	Hotel	Barbarian Honor Zulu
OCTOBER	NOVEMBER	DECEMBER	JANUARY
Cobra Chindit Old State Bldg O’Ryan Lima		Danger	Courage Abu Naji

BRAC4IRAQ Report

As of: 10 Jul 05

FOBs Closed since TOA: 18

FOBs Remaining: 91 (+4 CSCs, 4 DetFac)

Closures Pending(<100 days)

<u>Name</u>	<u>MND</u>	<u>Iraqi</u>	<u>MiTT</u>	<u>Disposition</u>	<u>Transfer</u>
Omaha	(NC)	1/1/4	Yes	Remagan	31JUL
Hotel	(W)	ISF	No	Duke	28AUG
Zulu	(CS)	3/3/8	No	Redeploy	01SEP
Scunion	(NC)	1/1/5	Yes	MNF-W	15JUL
Dagger	(NC)	4 DIV	Yes	Speicher	31JUL
Qurna	(SE)	1/1/10	Yes	Redeploy	15JUL
Barbarian	(NC)	IPS	No	Warrior	30SEP
Honor	(B)	5/6	Yes	Liberty	28SEP
Lima	(W)			Kalsu	01OCT

Closure Nominations

<u>Name</u>	<u>MND</u>	<u>Iraqi</u>	<u>MiTT</u>	<u>Transfer</u>
Chindit	(SE)	2/1/10	No	01OCT
OSB	(SE)	MoF	No	01OCT
O'Ryan		30 BDE		30OCT
Cobra	(NC)	3/2/5	Yes	OCT
Danger	(NC)		No	DEC
Courage	(NW)			JAN
Abu Naji	(SE)	1/4/10	No	JAN

Working Issues

- Danger Closure Plan
- ISF Infrastructure Expansion
- Coalition Commitments
- OIF 05-07/06-08 Force Footprint

	Coalition Camps	ISF Camps
MND-SE	15	8
MND-CS	4	7
MND-B	12	10
MNF-W	26	13
MND-NC	25	18
MND-NW	8	9
MND-NE	1	4
Detention Facility	4	
Convoy Support Center	4	

Magic Basing Number From 134 to 92

- Base Camp Management Report (BCMR)
 - 134 Locations
- 1st COSCOM FOB (-1) Vanguard not counted =133
- Victory Base counted as (1) and not (6) so (-5)= 128
- MND-NC Locations considered closed (7)=121
 - Fortitude, Midland, Tinderbox, Dibbis, PB A (Crazy Horse), Stone, and Magic Mountain.
- MNF-W (-1) FOB Wolf=120
- MNF-NW (-3)=117
 - Retrans South, Round Top, and Sinjar Retrans.
- Coalition Munitions Clearance (-4)=113
 - Arlington, Buckmaster, Jaguar, and Paladin
- Relay Points(-14)=99
- Detention Facilities (-4)=95
 - Cropper, Bucca, Abu Ghraib, and Ashraf.
- Convoy Support Centers (-3)=92
 - Korean Village, Scania, and Cedar II



Foreign Excess Personal Property (FEPP) Transfer to Iraq

- MNC-I base consolidation plan identified the need to transfer to incoming Iraqi Security Forces certain excess life support equipment
- Jan 05 MNF-I began process to obtain approval to transfer Foreign Excess Personal Property (FEPP) from COBs/COLs to the Iraqi Government
- 15 June 05 DUSD LM&R approved delegation of authority to MNF-I for transfer of up to \$2M of FEPP per site for 23 sites.
- DCS R&S recognized by Joint Staff as CG, MNF-I agent to execute property transfer of each site by signing MOA with Iraqi Deputy General, Acquisition, Logistics and Infrastructure
- Prior to MNC-I unit departure maximum cross-leveling of property conducted, remaining FEPP is jointly inventoried and sub-hand receipted to Senior Iraqi officer of unit occupying site
- MNC-I administratively moves property to separate Property Book. Sub-Hand Receipted Inventory is provided to DCS R&S, MOA and inventory packets are presented by DCS R&S to Iraqi DG for joint signing and property transfer
- DCS R&S directs MNC to remove property from property books
- COBs/COLs pending property transfer
 - Independence
 - Volunteer
 - Dibbis
 - Justice
- Transfer pending coordinated concept brief to Iraqi Deputy General, Acquisition, Logistics and Infrastructure
- Draft MNF-I transfer procedure guidance is under MNF-I legal review. Final guidance will be submitted for inclusion to MNF-I Command Policy and Procedures
